
Sindh Municipal Services Delivery Program MONTHLY PROGRESS REPORT

(DECEMBER 2022)



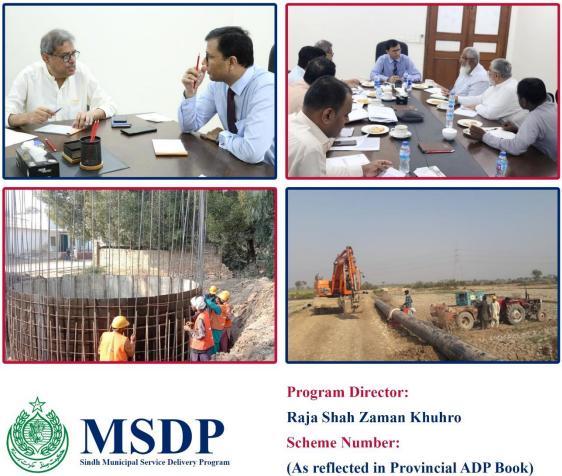

Program Director: Raja Shah Zaman Khuhro Scheme Number: (As reflected in Provincial ADP Book) ADP No. 2635/2022-23 Program Started: 2012 Execution of Work Started: March 2014 end date 30th September 2023

House No. D-18, Block-2 Kehkashan Clifton, Karachi www.msdp.sindh.gov.pk | Telephone # 021-35810017-18 | Fax # 021-35810019

Prepared by:	Monitoring & Evaluation Section MSDP
Verified by:	Technical & Finance Section MSDP
Submitted by:	Monitoring & Evaluation Section MSDP
Submitted to:	Pⅅ, M&E Cell and USAID/PAKISTAN
Program Directors:	Mr. Raja Shah Zaman Khuhro

Contents

1	INTRODUCTION	6
2	SUMMARY OF PROJECT ACTIVITIES (ALL COMPONENTS)	_7
3	OVERALL PROGRESS OF THE PROGRAM	_10
4	PROGRESS OF WATER SUPPLY PROJECT	_10
5	PROGRESS OF WASTE WATER PROJECT	_11
6	WATER SUPPLY & SEWERAGE CONNECTIONS	_13
7	FINANCIAL PROGRESS	_14
8	PICTORIAL OVERVIEW OF WASTE-WATER CONTRACT PACKAGES	_15
9	ENVIRONMENTAL COMPLIANCE AT SITE	_18
10	PROJECT GRIEVANCES REDRESSAL MECHANISM (GRM) OF SINDH-MSDP	_19
11	MEETINGS	_21
12	SITE VISITS	_23
13	WORKSHOP	25

List of Tables

Table 1: Summary of Project Activities 7
Table 2: Overall Progress of the Program 10
Table 3: Progress of Water Supply Project 10
Table 4: Physical Progress of Waste Water Project (Component wise) as of 31 st December 2022
Table 5: Pocket Wise/ Street Wise Progress of Waste Water as of 31 st December 2022 12
Table 6: Clamps & Extended Connections as of 31st December 2022
Table 7: Household Connections of Sewer System as of 31 st December 2022 13
Table 8: Complaints Statistics as of 31 st December 2022
Table 9: Summary Sheet of GRM. 20
Table 10: Summary of Daily Field Visit

Abbreviations

	Acronyms
MSDP	Municipal Services Delivery Program
USAID	United States Agency for International Development
WS	Water Supply
С&ЕННС	Clamps & Extended Household Connections
WW	Waste Water
LGSA	Local Government Strengthening Activity
EAS (DPC)	Energy Audit Study of Dhabeji Pumping Complex
IPC	Interim Payment Certificate
GRM	Grievances Redressal Mechanism
РСР	Pakistan Citizen's Portal
TCI	Techno Consultant International
PMU	Program Management Unit
PSU	Program Support Unit
IAP	Interim Payment Application
МСЈ	Municipal Committee Jacobabad
EM	Equipment & Machinery
BOQ	Bill of Quantities
AWS	Additional Water Supply

1 INTRODUCTION

This report reflects the Monthly Progress of December 2022, prepared by Sindh Municipal Services Delivery Program (MSDP). The report furnishes updates as of 31st December 2022.

1.1 Background of the Project

Name of Program	Sindh Municipal S	Services D	eliver	y Program			
Program Goal	Sustained improver	nent in m	unicip	al service delivery	to effectively address the		
	basic needs of citize	ens locate	d in sm	all and medium to	wns		
Foundation Year	2012						
	Activity Agreemen	nt signed	on 25	th April 2012 bet	ween USAID/Pakistan &		
	Government of Sind	dh					
Completion Year	September 2023 (E	xtension w	vas pre	viously granted in	the year 2020)		
Executing Partners	Government of Sindh						
Funds Committed	USAID	USD 66.00 Million					
	GoS	PKR 92	6.5 Mi	llion			
Total Funds	PKR 6,668.55 milli	on					
Organizational Structures	Program Steer Committee-P	-	Progr	am Management Unit-PMU	Program Support Unit- PSU		
Targeted Towns	1. Jacobabad 2. Joh	i 3. KN S	nah 4.	Shahdadkot 5. Qar	nbar 6. Mehar		
Components	Development	Compone Type-A Water Sup	1	Rehabilitation & Supply System	velopment Component Timprovement of Water in Jacobabad has been ded over to MCJ on 14-04-		
	(Type-E Sanitatio Waste Wa	on	Upgradation of Jacobabad town	ne Rehabilitation and Waste water system in has also started from hieved progress up to 78%		
		Waste		Type-C Solid Waste Management		over to Municipa 22.06.2019 in Jacobabad for har of this fleet, after for Jacobabad, re to other cities in	Machinery were handed l Committee Jacobabad on the Numaish Ground, ndling of Solid Waste. Out er retaining the machinery emaining were distributed e. Jacobabad (40), Thull ro (11), Shahdadkot (09), Tangwani (07).
	Soft	LGSA		Soft Component	21d March 2021 and all the		
		Energy Au Study of I			3 rd March 2021 and all the completed on 20 th October		

2 SUMMARY OF PROJECT ACTIVITIES (ALL COMPONENTS)

The overall consolidated status of each awarded contract is given below:

	Table 1: Summary of Project Activities								
Package Code	Package Name	Name of Construction Contractor	Contract Cost in	Date of Commencement	Date of completion extended up to	Status			
	INFRASTRUCTURE DEVELOPMENT: TYPE A (WATER SUPPLY)								
WS-01	Water Intake and Storage System	M/s Samad Khan Babar & Co	332,142,149	March 13 th , 2014	May 31 st , 2017	Completed Handed Over to MCJ on 22.05.2017			
WS-02	High Lift Pumping System and Rising Mains	M/s Shaikh Baz Khan & Brothers	639,589,414	March 13 th , 2014	November 17 th , 2016	Completed Handed Over to MCJ on 22.05.2017			
WS-03	Water Supply Transmission Loop	M/s Crescent Construction Company & KSB Pumps Company Ltd.	256,507,205	March 13 th , 2014	March 31 st , 2017	Completed Handed Over to MCJ on 14.04.2021			
WS-04	Water Distribution System Zone 1 & 2	M/s MAX-RITE Global Technologies (Pvt.) Ltd.	206,725,598	September 27 th , 2017	November 30 th , 2019	Completed Handed Over to MCJ on 14.04.2021			
WS-05	Water Distribution System Zone 3 & 4	M/s Matracon Pakistan (Pvt.) Limited	220,798,980	September 26 th , 2014	March 22 nd , 2019	Completed Handed Over to MCJ on 14.04.2021			
WS-06	Water Distribution System Zone 5 & 6	M/s Khan Mohammad & Co.	153,129,329	November 21 st , 2014	March 29 th , 2019	Completed Handed Over to MCJ on 14.04.2021			
WS-15	Rehabilitation & Extension of Existing Water Treatment Plant at Jacobabad	M/s Mohammad Iqbal Shaikh& Co.	201,894,354	November 11 th , 2015	March 29 th , 2019	Completed Handed Over to MCJ on 14.04.2021			
EM-11	Procurement and Installation of E&M Works	M/s Engineering Links International	125,560,528	May 18 th , 2017	March 22 nd , 2019	Completed Handed Over to MCJ on 14.04.2021			

		INFRASTRU	CTURE DEVELO	PMENT: TYPE B	(WASTE WATER)		
Package Code	Package Name	Name of Construction Contractor	Contract Cost	Expected Completion Cost	Date of Commencement	Date of completion/ extended up to	Status
WW-07	Rehabilitation & Up- Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone A	M/s Shafqat Traders & Mohammad Hasni Builders (JV)	594.634 Million	419.464 Million	February 11 th , 2020	31 st March, 2023	In Progress
WW-08	Rehabilitation & Up- Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone B	M/s N.K & Co	476.042 Million	343.406 Million	February 7 th , 2020	31 st March, 2023	In Progress
WW-09	Rehabilitation & Up- Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone C	M/s Kaim Khani & Brothers	476.566 Million	317.048 Million	February 7 th , 2020	31 st March, 2023	In Progress
WW-10	Rehabilitation & Up- Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone D	M/s Kaim Khani & Brothers	334.822 Million	334.758 Million	February 11 th , 2020	31 st March, 2023	In Progress
WW-12	Wastewater Treatment Plant Works Zone C	M/s Mohammad Iqbal Shaikh & Co.	359.38 Million	455.445 Million	February 4 th , 2021	31 st March, 2023	In Progress
WW-16	Enhancement of Sewerage Flow from Main Pumping House of Zone-A, B, C to their Oxidation Pond for Treatment purpose in Jacobabad	(To be Awarded)	394.707 Million (Lowest Quoted Cost)	394.800 Million	After completing all codal formalities the recommendation document hoisted on SPPRA Website on 28.10.2022. The award work is awaited for Revised Budget through PIL-11		2. The award of

Note: Extension of EOTs are under process.

INFRASTUCTURE DEVELOPMENT: TYPE C (SOLID WASTE MANAGEMENT)

Package Code	Package Name	Name of Construction Contractor	Contract Cost	Date of Commencement	Date of completion extended up to	Status
EM-14	Procurement of Equipment and Machinery for Improvement of Solid Waste Management System in Jacobabad	M/s Colibrative Heavy Industries (Pvt.) Limited	188,617,000	June 13 th , 2018	June 22 nd , 2019	Completed All the Equipment and Vehicles were distributed among Local Councils of Jacobabad, Thull, Ghari Khero, Shahdadkot, Sehwan & Tangwani towns.

	SOFT COMPONENT								
	ackage Code	Package Name	Name of Construction Contractor	Contract Cost in	Date of Commencement	Date of completion extended up to	Status		
		Local Government Strengthening Activity	M/s MDC (Pvt.) Ltd.	79,998,910	October 22 nd , 2019	August 31 st , 2021	Completed		
Ι	LGSA	Hiring of Training Consultant for required International Trainings for Capacity Building	M/s Stalwart Design Concepts	290,000	August 11 th , 2022	September 13 th , 2022	Training Deliverables/ToRs have been Completed		
	EAS of DPC	Energy Audit Study of the Dhabeji Pumping Station of KW&SB	M/s Techno-Consult International (Pvt.) Ltd. (Lead Firm), M/s Eleken Associates (JV Partner) & M/s WEE Pros GmbH- Germany (Associates)	49,200,400	March 3 rd , 2021	October 20 th , 2021	Completed		

3 OVERALL PROGRESS OF THE PROGRAM

S. No.	Components	ble 2: Overall Progre. Cost (PKR)	Status	Physical Progress	Weightage	Physical Progress as per weightage in %		
Α	INFRASTRUCTURE DEVELOPMENT							
i	Rehabilitation & Improvement of Water Supply System in Jacobabad	2,141,893,087	Completed	100%	44.15%	44.15%		
ii	Rehabilitation & Improvement of Sewerage Disposal & Treatment System Jacobabad	2,391,590,567	In Progress	78%	49.30%	38.45%		
iii	Solid Waste Management	188,617,000	Completed	100%	3.89%	3.89%		
В		SOFT CO	OMPONENT		•			
i	Local Government Strengthening Activity	80,072,910	Completed	100%	1.65%	1.65%		
ii	Energy Audit Study Of KW&SB Dhabeji Pumping Complex	49,200,400	Completed	100%	1.01%	1.01%		
	TOTAL	4,851,373,964				89.15%		
Overall	Overall physical progress of MSDP is: 89.15%							

Table 2: Overall Progress of the Program

4 PROGRESS OF WATER SUPPLY PROJECT

Table 3: Progress of Water Supply Project

Package Code	Package Name	Physical Progress	Financial Progress	Status
WS-01	Water Intake and Storage System	100%	100%	22.05.2017
WS-02	High Lift Pumping System and Rising Mains	100%	100%	22.03.2017
WS-03	Water Supply Transmission Loop	100%	100%	
WS-04 R	Water Distribution System Zone 1 & 2	100%	100%	
WS-05	Water Distribution System Zone 3 & 4	100%	100%	Completed &
WS-06	Water Distribution System Zone 5 & 6	100%	100%	handed over to MCJ on
WS-15	Rehabilitation & Extension of Existing Water Treatment Plant at Jacobabad	100%	100%	14.04.2021
EM-11	Procurement and Installation of E&M Works	100%	100%	

5 PROGRESS OF WASTE WATER PROJECT

The waste water components are currently in execution phase under the supervision of M/s RCC Consultant who acts as the Engineer and TCI appointed by the USAID as Third-Party monitoring.


5.1 Physical & Financial Progress of Waste Water Component

The detailed progress under each sub-component of waste water is given as under:

Packages Number Code	Table 4: Physical Progress of Waste Water Proj Packages Name	Physical Progress as per BOQ up to 31 st December 2022	Overall Physical Progress as per Site up to 31 st December 2022	Overall Financial Progress as per contract up to 31 st December 2022
WW-07	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-A at Jacobabad,	79.85%	85.71%	34.04%
WW-08	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-B at Jacobabad,	64.72%	85.72%	38.19%
WW-09	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-C at Jacobabad,	55.91%	77.05%	27.37%
WW-10	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-D at Jacobabad,	58.72%	72.69%	43.31%
WW-12	Wastewater Treatment Plant Works Zone D	53.08%	68.83%	41.04%
Overall Phy	vsical Progress	62.45%	78%	36.79%

Table 4: Physical Progress of Waste Water Project (Component wise) as of 31st December 2022

Note: Overall Physical Progress based on workable quantities as per site identified by the Engineer-RCC Consultant

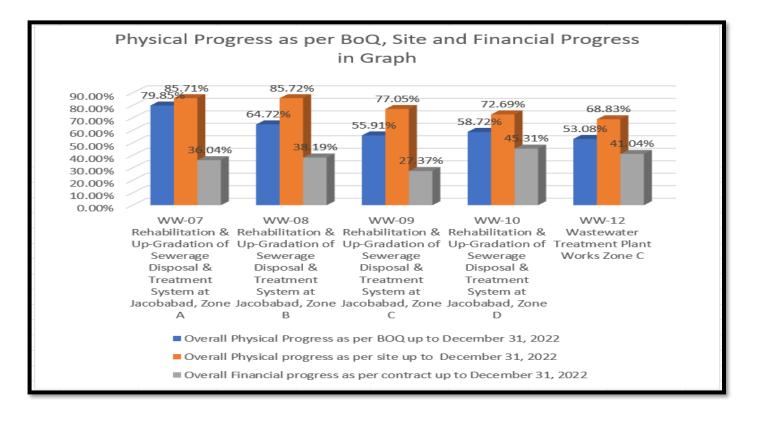

	_		Wise Prog	ress		Street Drain Wise Progress			
Packages/ Zone	Total Numbers of Pockets In each zone	Pocket wise work has started/ In- progress (under 50%)	Pocket wise then 50% work has been done	Completed & Connected Pocket	Yet not started	Total Streets/ Drains	Completed Streets	In- progress streets	Yet not started
1	2	3	4	5	6	7	8	9	10
WW-07 Zone - A	17	2	3	11	1	816	446	21	349
WW-08 Zone -B	21	2	2	17	0	580	290	6	284
WW-09 Zone -C	11	3	2	6	0	399	261	5	133
WW-10 Zone -D	8	1	1	5	1	344	313	6	25
Total	57	8	8	39	2	2139	1310	38	791

Table 5: Pocket Wise/ Street Wise Progress of Waste Water as of 31st December 2022

6 WATER SUPPLY & SEWERAGE CONNECTIONS

6.1 Clamps & Extended Household Connections (Updated by Municipal Committee Jacobabad as on 31.12.2022)

The current position of clamps and extended household connections installed up to 31.12.2022 are given below:

S. No.	Zone	Total Registration	Connection Provided by MC Jacobaba after Handing/Taking	
01	Zone-01	3445	3295	
02	Zone-02	1904	1699	
03	Zone-03	3161	2711	
04	Zone-04	1700	1422	
05	Zone-05	2369	1902	
06	Zone-06	3363	1730	
07	AWS-3 (Missing Street in above different water supply Zones)	1062	1062	
08	Zone 5 -A (Through WS-13)	1566	Nil	
	Total	18570	13821	

Table 6: Clamps & Extended Connections as of 31st December 2022

6.2 Data of Household Connections of Sewer System as of 31st December 2022

Table 7: Household Connections of Sewer System as of 31st December 2022

ZONE	Previous House connections till 30 th November 2022	New No. of House connections in the Month of December 2022	Total number of House connections till 31 st December 2022		
Α	4246	15	4261		
В	2322	35	2357		
С	2567	0	2567		
D	1564	0	1564		
	Total		10,749		

7 FINANCIAL PROGRESS

7.1 Status of IPCs Payment up to December 2022 (Running Activities)

Packages Number	Packages Name	Financial Progress (up to 31.12.2022) (in % age)	Total Payment made in the month of December 2022 (PKR)	Total Payment made till 31 st December 2022 (PKR)
WW-07	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone A	36.04%	8,819,465	214,310,132
WW-08	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone B	38.19%	Nil	181,789,619
WW-09	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone C	27.37%	Nil	130,426,692
WW-10	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone D	45.31%	5,015,705	151,721,839
WW-12	Wastewater Treatment Plant Works Zone C	41.04%	Nil	147,482,590
A&E Firm (Cost revised)	M/s RCC Consultant	79.89%	4,093,000	104,520,233
	Total	44.6%	17,928,170	930,251,105

8 PICTORIAL OVERVIEW OF WASTE-WATER CONTRACT PACKAGES



WW-07 (Zone-A) Excavation for Boundary wall of Revenue Colony disposal work is in progress

WW-08 (Zone-B) Brick Masonry work of drain is in progress at street No 2-C Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Brick Masonry of drain is in progress at street No. 4-A Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Excavation of drain work is in progress at street No. 7-C Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Steel Fixing Reinforcement Sump work is in progress at Al Murtaza Colony Jacobabad



WW-12 Rising main 500 dia work is in progress from Shamb-e-Shah to Noor Wah Jacobabad



Sindh Municipal Services Delivery Program-Monthly Progress Report-December 2022

9 ENVIRONMENTAL COMPLIANCE AT SITE

Regarding environmental compliance and monitoring at site, the draft modified EDF-EMMP document is referred. Monitoring on-site was carried out for each contract package as per the corresponding EMMP. The draft modified EDF-EMMP document is yet to be approved by USAID. The environmental compliance report is separately submitted to USAID.



To check the Air Pollution level with the help of Formaldehyde Detector



To check the Noise Pollution level with the help of (Digital Sound level Meter).



Monitoring of Air Pollution level during execution of work at Zone A Yard with the help of Formaldehyde



Monitoring of Air Pollution level with help of Formaldehyde Detector

10 PROJECT GRIEVANCES REDRESSAL MECHANISM (GRM) OF SINDH-MSDP

The Sindh-MSDP is enthusiastic and motivated to address/ resolve the grievances of citizens of Jacobabad, Sindh. It is pivotal for any democratic society that the people (end users) and their ideas be put in first place. This makes the Grievances Redressal a very important task. The Sindh-MSDP effectively ensures the systematic resolution of citizen grievances through a transparent and efficient manner on the fast track. Presently, a dual system is prevailing for Project's Grievances Redressal Mechanism; Pakistan Citizen's Portal (PCP); and MSDP's internal mechanism established at designated Project Support Unit Jacobabad and Project Management Unit. This task demands dedicated and concentrated efforts in the right direction to bring sustainable change. It is not out of place to mention that Sindh-MSDP has embarked effectively for providing higher level of service delivery to urban and peri-urban population of project area for enhanced quality of life.

Table 8: Complaints Statistics as of 31st December 2022								
Pakistan Citizen's Portal (PCP)								
Total Complaints received up toComplaints ResolvedIn-progress								
December 2022 Complaints								
89	89	0						
Grievances Redressal Mechanism (GRM) for Project Activities								
97 91 06								

The above statistical illustration is an overall glimpse of grievances received and resolved through Pakistan Citizen Portal (PCP) and Grievances Redressal Mechanism (GRM) during the month of December 2022 regarding service delivery. It is aimed that the MSDP team will continue to work dedicatedly day in and day out to ensure the rapid Redressal of Citizens Grievances.

In order to address the issues highlighted by general public regarding connectivity, de-silting, placement of slabs on drains and lifting of dismantled/waste material from site etc. the five (05) Sub Engineers of Program Support Unit have been mobilized. They visit the field on regular basis and report the on-ground situation on a checklist/ proforma. The Assistant Director (Design)/Incharge PSU & Assistant Director (Execution) Program Support Unit compiles the observations and shares the same with Resident Engineer, RCC Consultant for their timely redressal.

10.1 Grievance's Redressal Mechanism (GRM)

Table 9: Summary Sheet of GRM Grievances Redressal Mechanism (GRM) SUMMARY SHEET

Progress up to 31st December 2022

S. No.	NATURE /CATEGORY OF COMPLAINT	TOTAL COMPLAINTS RECEVIED		TOTAL COMPLANTS RESOLVED		TOTAL COMPLAINTS PENDING		REASONS OF PENDENCY	REMARKS			
		Dec 2022	Sep 2021 to Dec 2022	Total	Dec 22	Sep 2021 to Dec 2022	Total	Dec 22	Sep 2021 to Dec 2022	Total		
1	2	3	4	5	6	7	8	9	10	11	12	13
1	Water Supply	0	11	11	0	11	11	0	0	0	-	-
2	Waste Water	2	84	86	0	80	80	0	6	6	Work in Progress	RCC was requested to resolve pending GRM at war- footing basis
G	rand Total	2	95	97	0	91	91	0	6	6		

10.2 Summary of daily field visit reports of all packages by Sub Engineers

Summary of daily field visit reports of all contract packages

(WW-07, 08, 09 & 10)

Table 10: Summary of Daily Field Visit

S. No.	Name of Sub Engineer	Name of Zone	Total sites visited by concerned Sub Engineer
1.	Mr. Abrar Ahmed Thaheem & Mr. Anis-ur-Rehman Khoso	WW-07 (Zone A)	88
2.	Mr. Mudassar Ali Rajput	WW-08 (Zone B)	105
3.	Mr. Asghar Abbas Sadhayo	WW-09 (Zone C)	52
4.	Mr. Tufail Ahmed Soomro	WW-10 (Zone D)	86
	Total		331

11 MEETINGS

11.1 In-house meeting on improvement of Sindh MSDP Website

An in-house meeting of the officers of Sindh Municipal Services Delivery Program, Planning & Development Department, Government of Sindh was held under the Chairmanship of Director General (works) MSDP on 1st December 2022 in the Committee room of Sindh MSDP to discuss the regular update of Sindh MSDP website <u>www.msdp.sindh.gov.pk.</u>

At the outset, the Director General (Works) welcomed the participants and emphasized the regular update of the website. He reminded all the participants that USAID is a partner of MSDP therefore the uploaded text, data, pictures, and any activities should be present by informing USAID. Following officers of Sindh MSDP Mr. S.M Shakaib Director General (Works), Ms. Uzaima Nasir Director (F&C), Mr. Rahmatullah Pirzada Director (M&E), Babar Ismail Palijo Procurement Specialist/Deputy Director (Design), Mr. Sanaullah Soomro Deputy Director (Execution), Mr. Muhammad Aslam Memon Assistant Director (HRD), Mr. Yahya Noor Ansari Assistant Director (Procurement), Mr. Muhammad Faisal Saeed Assistant Director (M&E), and Mr. Gulab Tanwari Assistant Director (Database) attended the meeting.

11.2 Follow up meeting with Waste Water Contractors

A follow up meeting for the monitoring of progress activities at site was held with the Waste Water Contractors under the Chairmanship of the Director General (Works) MSDP on 13th December 2022 in the Committee room of Sindh MSDP to discuss the course of action and the spent plan for the completion of the project. At the outset, Director General (Works) welcomed the participants and communicated that the follow-up meetings for the review of site activities and issues will be held either Tuesday or Monday every week.



However, Director General (Works) MSDP also conveyed that in such weekly meetings instead of all contractors may only the contractors of the respective sites, where there is slow progress will be called for the meeting. After detailed deliberation, asked M/s RCC Consultants for a month wise spent plan. It was also informed that the project fund is being arranged by USAID and there is lapsable fund as there is not much time left to avoid lapse.



The Director General (Works) MSDP emphasized the close coordination on a daily basis between all project Managers and Project Support team is needed to get the possible outcome/targets. Mr. Babar Ismail Palijo Procurement Specialist/Deputy Director (Design), Mr. Murtaza Ali Jakhar Deputy Director (Reforms), Ms. Saba Zehra Assistant Director (GIS/MIS), Mr. Basheer Ahmed Resident Engineer M/s RCC Consultants Mr. Hamid Naveed K.K Brothers, Mr. Fida Hussain K.K Brothers and Mr. Nisar A Khan N.K & Company were present in the meeting. However, Mr. Babar Sarki Assistant Director (Design)/Incharge PSU-MSDP, Mr. Waqar Ali Kalwar Assistant Director (Execution) PSU-MSDP Jacobabad, Mr. Asif Rind Project Manager WW-07, Mr. Muhabbat Mangi Project Manager WW-08, and Mr. Mumtaz Tunio Project Manager WW-09 participated in the meeting virtually.

12 SITE VISITS

12.1 Site visit at WW-12 Raising Main Noor Wah Jacobabad

On 8th December 2022 Assistant Director (Design)/Incharge PSU Jacobabad and Mr. Bashir Ahmed Resident Engineer M/s RCC Consultants, Mr. Mubashir Abbasi Assistant Resident Engineer Ms. RCC Consultants Mr. Ramzan Memon Project manager WW-12, Mr. Tufail Soomro Sub Engineer Project Support Unit Jacobabad visited site WW-12 to monitor progress of Laying of pipeline work of 500 mm diameter PE Pipeline raising main Noor Wah route. During the visit Incharge PSU reiterated for timely completion of all remaining works on war footing basis.



12.2 Site visit at WW-08 (Zone B) Gulab Machi Goth Pumping Station

On 14th December 2022 Mr. Babar Sarki Assistant Director/Incharge PSU-MSDP Jacobabad along with Mr. Waqar Ali Kalwar Assistant Director (Execution) MSDP, Mr. Bashir Ahmed Resident Engineer M/s RCC Consultants and Mr. Mubashir Abbasi Assistant Resident Engineer M/s RCC Consultants visited the site at WW-08 (Zone B) Gulab Machi Goth Pumping Station Jacobabad. During the visit Incharge PSU-MSDP Jacobabad reiterates that the dewatering activities will be completed on priority basis and work will be resumed very soon.



12.3 Site visit at WW-12 Noor Wah Rising Main route Jacobabad

On 23rd December 2022 Mr. Babar Sarki Assistant Director/Incharge PSU-MSDP Jacobabad along with Mr. Bashir Ahmed Resident Engineer M/s RCC Consultants and Mr. Mubashir Abbasi Assistant Resident Engineer M/s RCC Consultants, Mr. Ramzan Memon Project Manager WW-12 and Mr. Tufail Soomro Sub Engineer PSU MSDP visited the site to witness the progress of 500 mm diameter PE Pipeline Rising Main Noor Wah route Jacobabad. During the visit Mr. Basheer Nahiyoon Resident Engineer M/s RCC Consultants informed the progress of excavation of trench for laying of pipeline at Noor Wah Rising Main route Jacobabad.



12.4 Site visit at WW-07 (Zone A) Civil Court Chowk Jacobabad

On 23rd December 2022 Mr. Babar Sarki Assistant Director/Incharge PSU-MSDP Jacobabad along with Mr. Bashir Ahmed Resident Engineer M/s RCC Consultants and Mr. Mubashir Abbasi Assistant Resident Engineer M/s RCC Consultants visited the site at WW-07 (Zone B) Civil Court Chowk Jacobabad to witness the drain connectivity to BLISS (Primary Drain).



13 WORKSHOP

13.1 Audit Planning Workshop, M&E and Project Impact Evaluation Workshops

The Program Director Sindh MSDP, Director (Finance & Compliance), Procurement Specialist/ Deputy Director Design) and Assistant Director (Finance) Sindh MSDP attended the following workshops during the month of December 2022.

S No.	Name	Designation	From	То	Name of Workshop	Institute & Venue
1.	Mr. Raja Shah Zaman Khuhro	Program Director			Workshop	venue
2.	Ms. Uzaima Director Nasir (F&C)		21 st December 2022	22 nd December 2022	G2G Audit Planning Workshop for the G2G Implementing	USAID Pakistan Islamabad
3.	Mr. M. Faisal Saeed	Assistant Director (Finance)			Partners	
4.	Ms. Uzaima Nasir	Director (F&C)	27 th December 2022	29 th December 2022	Monitoring, Evaluation and Research Roundtable-An Institutional Approach to Enhanced SDGs Reporting in Pakistan	Ministry of Planning & development & Special Initiative (Sustainable Development Goals Sections) Government of Pakistan Islamabad
5.	Mr. Babar Ismail Palijo	Procurement Specialist/ Deputy Director (Design)			Project Impact & Evaluation	Institute of Business Administration Karachi





Program Management Unit

Sindh Muincipal Service Delivery Program

D-18 Block-2 Clifton Karachi

Pakistan

Tel No. 021-35810017-18 | Fax No. 021-35810019

www.msdp.sindh.gov.pk
