

## Sindh Municipal Services Delivery Program

# MONTHLY PROGRESS REPORT

(JANUARY 2023)



**MSDP**  
Sindh Municipal Service Delivery Program



**USAID**  
FROM THE AMERICAN PEOPLE

**Program Director:**

**Raja Shah Zaman Khuhro**

**Scheme Number:**

**(As reflected in Provincial ADP Book)**

**ADP No. 2635/2022-23**

**Program Started: 2012**

**Execution of Work Started:**

**March 2014 end date 30<sup>th</sup> September 2023**

House No. D-18, Block-2 Kehkashan Clifton, Karachi  
www.msdp.sindh.gov.pk | Telephone # 021-35810017-18 | Fax # 021-35810019

**Prepared by:** Monitoring & Evaluation Section MSDP  
**Verified by:** Technical & Finance Section MSDP  
**Submitted by:** Monitoring & Evaluation Section MSDP  
**Submitted to:** P&DD, M&E Cell and USAID/PAKISTAN  
**Program Director:** Mr. Raja Shah Zaman Khuhro

## Contents

<b>1</b>	<b>INTRODUCTION</b>	<b>6</b>
<b>2</b>	<b>SUMMARY OF PROJECT ACTIVITIES (ALL COMPONENTS)</b>	<b>7</b>
<b>3</b>	<b>OVERALL PROGRESS OF THE PROGRAM</b>	<b>10</b>
<b>4</b>	<b>PROGRESS OF WATER SUPPLY PROJECT</b>	<b>10</b>
<b>5</b>	<b>PROGRESS OF WASTE WATER PROJECT</b>	<b>11</b>
<b>6</b>	<b>WATER SUPPLY &amp; SEWERAGE CONNECTIONS</b>	<b>13</b>
<b>7</b>	<b>FINANCIAL PROGRESS</b>	<b>14</b>
<b>8</b>	<b>PICTORIAL OVERVIEW OF WASTE-WATER CONTRACT PACKAGES</b>	<b>15</b>
<b>9</b>	<b>ENVIRONMENTAL COMPLIANCE AT SITE</b>	<b>26</b>
<b>10</b>	<b>PROJECT GRIEVANCES REDRESSAL MECHANISM (GRM) OF SINDH-MSDP</b>	<b>27</b>
<b>11</b>	<b>MEETINGS</b>	<b>29</b>
<b>12</b>	<b>TRAINING</b>	<b>33</b>

## List of Tables

Table 1: Summary of Project Activities . . . . .	7
Table 2: Overall Progress of the Program . . . . .	10
Table 3: Progress of Water Supply Project . . . . .	10
Table 4: Physical Progress of Waste Water Project (Component wise) as of 31 <sup>st</sup> January 2023	11
Table 5: Pocket Wise/ Street Wise Progress of Waste Water as of 31 <sup>st</sup> January 2023 . . . . .	12
Table 6: Clamps & Extended Connections as of 31 <sup>st</sup> January 2023 . . . . .	13
Table 7: Household Connections of Sewer System as of 31 <sup>st</sup> January 2022 . . . . .	13
Table 8: Complaints Statistics as of 31 <sup>st</sup> January 2023 . . . . .	27
Table 9: Summary Sheet of GRM . . . . .	28
Table 10: Summary of Daily Field Visit . . . . .	28

## Abbreviations

<b>Acronyms</b>	
<b>MSDP</b>	Municipal Services Delivery Program
<b>USAID</b>	United States Agency for International Development
<b>WS</b>	Water Supply
<b>C&amp;EHHC</b>	Clamps & Extended Household Connections
<b>WW</b>	Waste Water
<b>LGSA</b>	Local Government Strengthening Activity
<b>EAS (DPC)</b>	Energy Audit Study of Dhabeji Pumping Complex
<b>IPC</b>	Interim Payment Certificate
<b>GRM</b>	Grievances Redressal Mechanism
<b>PCP</b>	Pakistan Citizen's Portal
<b>TCI</b>	Techno Consultant International
<b>PMU</b>	Program Management Unit
<b>PSU</b>	Program Support Unit
<b>IAP</b>	Interim Payment Application
<b>MCJ</b>	Municipal Committee Jacobabad
<b>EM</b>	Equipment & Machinery
<b>BOQ</b>	Bill of Quantities
<b>AWS</b>	Additional Water Supply

# 1 INTRODUCTION

This report reflects the Monthly Progress of January 2023, prepared by Sindh Municipal Services Delivery Program (MSDP). The report furnishes updates as of 31<sup>st</sup> January 2023.

## Background of the Project

<b>Name of Program</b>	<b>Sindh Municipal Services Delivery Program</b>		
<b>Program Goal</b>	Sustained improvement in municipal service delivery to effectively address the basic needs of citizens located in small and medium towns		
<b>Foundation Year</b>	2012 Activity Agreement signed on 25 <sup>th</sup> April 2012 between USAID/Pakistan & Government of Sindh		
<b>Completion Year</b>	September 2023 (Extension was previously granted in the year 2020)		
<b>Executing Partners</b>	Government of Sindh		
<b>Funds Committed</b>	<b>USAID</b>	USD 66.00 Million	
	<b>GoS</b>	PKR 926.5 Million	
<b>Total Funds</b>	PKR 6,668.55 million		
<b>Organizational Structures</b>	Program Steering Committee-PSC	Program Management Unit-PMU	Program Support Unit-PSU
<b>Targeted Towns Components</b>	1. Jacobabad 2. Johi 3. KN Shah 4. Shahdadkot 5. Qambar 6. Mehar		
	Infrastructure Development Component	Components Type-A Water Supply	Infrastructure Development Component Rehabilitation & Improvement of Water Supply System in Jacobabad has been completed & handed over to MCJ on 14.4.2021
		Type-B Sanitation (Waste Water)	Work for the Rehabilitation and Upgradation of Waste water system in Jacobabad town has also started from March 2020 and achieved progress up to 78%.
		Type-C Solid Waste Management	Equipment and Machinery were handed over to Municipal Committee Jacobabad on 22.06.2019 in the Numaish Ground, Jacobabad for handling of Solid Waste. Out of this fleet, after retaining the machinery for Jacobabad, remaining were distributed to other cities i.e. Jacobabad (40), Thull (12), Garhi Khairo (11), Shahdadkot (09), Sehwan (09) and Tangwani (07).
	Soft Component	LGSA	The reports & manuals developed under LGSA has been disseminated to relevant stakeholders (P&DD, LG&HTP, Training & Management wing of SGA&CD, R&T Wing P&DD, Sindh Civil Services & Local Govt. Academy, Deputy Commissioner Jacobabad, Administrator MC Jacobabad, MCs of six towns i.e. Jacobabad, Qambar, Shahdadkot, K.N Shah, Mehar and Johi.
Energy Audit Study of DPC		Work initiated on 3 <sup>rd</sup> March 2021 and all the deliverables are completed on 20 <sup>th</sup> October 2021.	

## 2 SUMMARY OF PROJECT ACTIVITIES (ALL COMPONENTS)

The overall consolidated status of each awarded contract is given below:

Table 1: Summary of Project Activities

Package Code	Package Name	Name of Construction Contractor	Contract Cost in	Date of Commencement	Date of completion extended up to	Status
<b>INFRASTRUCTURE DEVELOPMENT: TYPE A (WATER SUPPLY)</b>						
<b>WS-01</b>	Water Intake and Storage System	M/s Samad Khan Babar & Co	332,142,149	March 13 <sup>th</sup> , 2014	May 31 <sup>st</sup> , 2017	Completed Handed Over to MCJ on 22.05.2017
<b>WS-02</b>	High Lift Pumping System and Rising Mains	M/s Shaikh Baz Khan & Brothers	639,589,414	March 13 <sup>th</sup> , 2014	November 17 <sup>th</sup> , 2016	Completed Handed Over to MCJ on 22.05.2017
<b>WS-03</b>	Water Supply Transmission Loop	M/s Crescent Construction Company & KSB Pumps Company Ltd.	256,507,205	March 13 <sup>th</sup> , 2014	March 31 <sup>st</sup> , 2017	Completed Handed Over to MCJ on 14.04.2021
<b>WS-04</b>	Water Distribution System Zone 1 & 2	M/s MAX-RITE Global Technologies (Pvt.) Ltd.	206,725,598	September 27 <sup>th</sup> , 2017	November 30 <sup>th</sup> , 2019	Completed Handed Over to MCJ on 14.04.2021
<b>WS-05</b>	Water Distribution System Zone 3 & 4	M/s Matracon Pakistan (Pvt.) Limited	220,798,980	September 26 <sup>th</sup> , 2014	March 22 <sup>nd</sup> , 2019	Completed Handed Over to MCJ on 14.04.2021
<b>WS-06</b>	Water Distribution System Zone 5 & 6	M/s Khan Mohammad & Co.	153,129,329	November 21 <sup>st</sup> , 2014	March 29 <sup>th</sup> , 2019	Completed Handed Over to MCJ on 14.04.2021
<b>WS-15</b>	Rehabilitation & Extension of Existing Water Treatment Plant at Jacobabad	M/s Mohammad Iqbal Shaikh & Co.	201,894,354	November 11 <sup>th</sup> , 2015	March 29 <sup>th</sup> , 2019	Completed Handed Over to MCJ on 14.04.2021
<b>EM-11</b>	Procurement and Installation of E&M Works	M/s Engineering Links International	125,560,528	May 18 <sup>th</sup> , 2017	March 22 <sup>nd</sup> , 2019	Completed Handed Over to MCJ on 14.04.2021

**INFRASTRUCTURE DEVELOPMENT: TYPE B (WASTE WATER)**

<b>Package Code</b>	<b>Package Name</b>	<b>Name of Construction Contractor</b>	<b>Contract Cost</b>	<b>Expected Completion Cost</b>	<b>Date of Commencement</b>	<b>Date of completion/ extended up to</b>	<b>Status</b>
<b>WW-07</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone A	M/s Shafqat Traders & Mohammad Hasni Builders (JV)	594.634 Million	419.464 Million	February 11 <sup>th</sup> , 2020	31 <sup>st</sup> March, 2023	In Progress
<b>WW-08</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone B	M/s N.K & Co	476.042 Million	343.406 Million	February 7 <sup>th</sup> , 2020	31 <sup>st</sup> March, 2023	In Progress
<b>WW-09</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone C	M/s Kaim Khani & Brothers	476.566 Million	317.048 Million	February 7 <sup>th</sup> , 2020	31 <sup>st</sup> March, 2023	In Progress
<b>WW-10</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone D	M/s Kaim Khani & Brothers	334.822 Million	334.758 Million	February 11 <sup>th</sup> , 2020	31 <sup>st</sup> March, 2023	In Progress
<b>WW-12</b>	Wastewater Treatment Plant Works Zone C	M/s Mohammad Iqbal Shaikh & Co.	359.38 Million	455.445 Million	February 4 <sup>th</sup> , 2021	31 <sup>st</sup> March, 2023	In Progress
<b>WW-16</b>	Enhancement of Sewerage Flow from Main Pumping House of Zone-A, B, C to their Oxidation Pond for Treatment purpose in Jacobabad	(To be Awarded)	394.707 Million (Lowest Quoted Cost)	394.800 Million	After completing all codal formalities the recommendation document hoisted on SPPRA Website on 28.10.2022. Letter of Acceptance has also been issued by Sindh MSDP on 7.12.2022. The award of work is awaited for Revised Budget through PIL-11		



### INFRASTRUCTURE DEVELOPMENT: TYPE C (SOLID WASTE MANAGEMENT)

Package Code	Package Name	Name of Construction Contractor	Contract Cost	Date of Commencement	Date of completion extended up to	Status
<b>EM-14</b>	Procurement of Equipment and Machinery for Improvement of Solid Waste Management System in Jacobabad	M/s Colibrative Heavy Industries (Pvt.) Limited	188,617,000	June 13 <sup>th</sup> , 2018	June 22 <sup>nd</sup> , 2019	Completed All the Equipment and Vehicles were distributed among Local Councils of Jacobabad, Thull, Ghari Khoro, Shahdaktot, Sehwan & Tangwani towns.

### SOFT COMPONENT

Package Code	Package Name	Name of Construction Contractor	Contract Cost in	Date of Commencement	Date of completion extended up to	Status
<b>LGSA</b>	Local Government Strengthening Activity	M/s MDC (Pvt.) Ltd.	79,998,910	October 22 <sup>nd</sup> , 2019	August 31 <sup>st</sup> , 2021	Completed
	Hiring of Training Consultant for required International Trainings for Capacity Building	M/s Stalwart Design Concepts	290,000	August 11 <sup>th</sup> , 2022	September 13 <sup>th</sup> , 2022	Training Deliverables/ToRs have been Completed
<b>EAS of DPC</b>	Energy Audit Study of the Dhabeji Pumping Station of KW&SB	M/s Techno-Consult International (Pvt.) Ltd. (Lead Firm), M/s Eleken Associates (JV Partner) & M/s WEE Pros GmbH- Germany (Associates)	49,200,400	March 3 <sup>rd</sup> , 2021	October 20 <sup>th</sup> , 2021	Completed

### 3 OVERALL PROGRESS OF THE PROGRAM

Table 2: Overall Progress of the Program

S. No.	Components	Cost (PKR)	Status	Physical Progress	Weightage	Physical Progress as per weightage in %
<b>A</b>	<b>INFRASTRUCTURE DEVELOPMENT</b>					
i	Rehabilitation & Improvement of Water Supply System in Jacobabad	2,141,893,087	Completed	100%	44.15%	44.15%
ii	Rehabilitation & Improvement of Sewerage Disposal & Treatment System Jacobabad	2,391,590,567	In Progress	79%	49.30%	38.95%
iii	Solid Waste Management	188,617,000	Completed	100%	3.89%	3.89%
<b>B</b>	<b>SOFT COMPONENT</b>					
i	Local Government Strengthening Activity	80,072,910	Completed	100%	1.65%	1.65%
ii	Energy Audit Study Of KW&SB Dhabeji Pumping Complex	49,200,400	Completed	100%	1.01%	1.01%
	<b>TOTAL</b>	<b>4,851,373,964</b>				<b>89.65%</b>
<b>Overall physical progress of Sindh MSDP is: 89.65%</b>						

### 4 PROGRESS OF WATER SUPPLY PROJECT

Table 3: Progress of Water Supply Project

Package Code	Package Name	Physical Progress	Financial Progress	Status
<b>WS-01</b>	Water Intake and Storage System	100%	100%	22.05.2017
<b>WS-02</b>	High Lift Pumping System and Rising Mains	100%	100%	
<b>WS-03</b>	Water Supply Transmission Loop	100%	100%	Completed & handed over to MCJ on 14.04.2021
<b>WS-04 (R)</b>	Water Distribution System Zone 1 & 2	100%	100%	
<b>WS-05</b>	Water Distribution System Zone 3 & 4	100%	100%	
<b>WS-06</b>	Water Distribution System Zone 5 & 6	100%	100%	
<b>WS-15</b>	Rehabilitation & Extension of Existing Water Treatment Plant at Jacobabad	100%	100%	
<b>EM-11</b>	Procurement and Installation of E&M Works	100%	100%	

## 5 PROGRESS OF WASTE WATER PROJECT

The waste water components are currently in execution phase under the supervision of M/s RCC Consultant who acts as the Engineer and TCI appointed by the USAID as Third-Party monitoring.

### 5.1 Physical & Financial Progress of Waste Water Component

The detailed progress under each sub-component of waste water is given as under:

Table 4: Physical Progress of Waste Water Project (Component wise) as of 31<sup>st</sup> January 2023

<b>Packages Number Code</b>	<b>Packages Name</b>	<b>Physical Progress as per BOQ up to 31<sup>st</sup> January 2023</b>	<b>Overall Physical Progress as per Site up to 31<sup>st</sup> January 2023</b>	<b>Overall Financial Progress as per contract up to 31<sup>st</sup> January 2023</b>
<b>WW-07</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-A at Jacobabad,	<b>79.85%</b>	<b>85.71%</b>	<b>36.04%</b>
<b>WW-08</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-B at Jacobabad,	<b>64.72%</b>	<b>86.94%</b>	<b>38.19%</b>
<b>WW-09</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-C at Jacobabad,	<b>55.91%</b>	<b>77.05%</b>	<b>27.37%</b>
<b>WW-10</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-D at Jacobabad,	<b>58.72%</b>	<b>72.69%</b>	<b>45.31%</b>
<b>WW-12</b>	Wastewater Treatment Plant Works Zone D	<b>53.08%</b>	<b>72.62%</b>	<b>41.04%</b>
<b>Overall Physical Progress</b>		<b>62.45%</b>	<b>79%</b>	<b>37.59%</b>

Note: Overall Physical Progress based on the basis of workable quantities as per site identified by the Engineer-RCC Consultant.

### Physical Progress as per BoQ, Site and Financial Progress in Graph

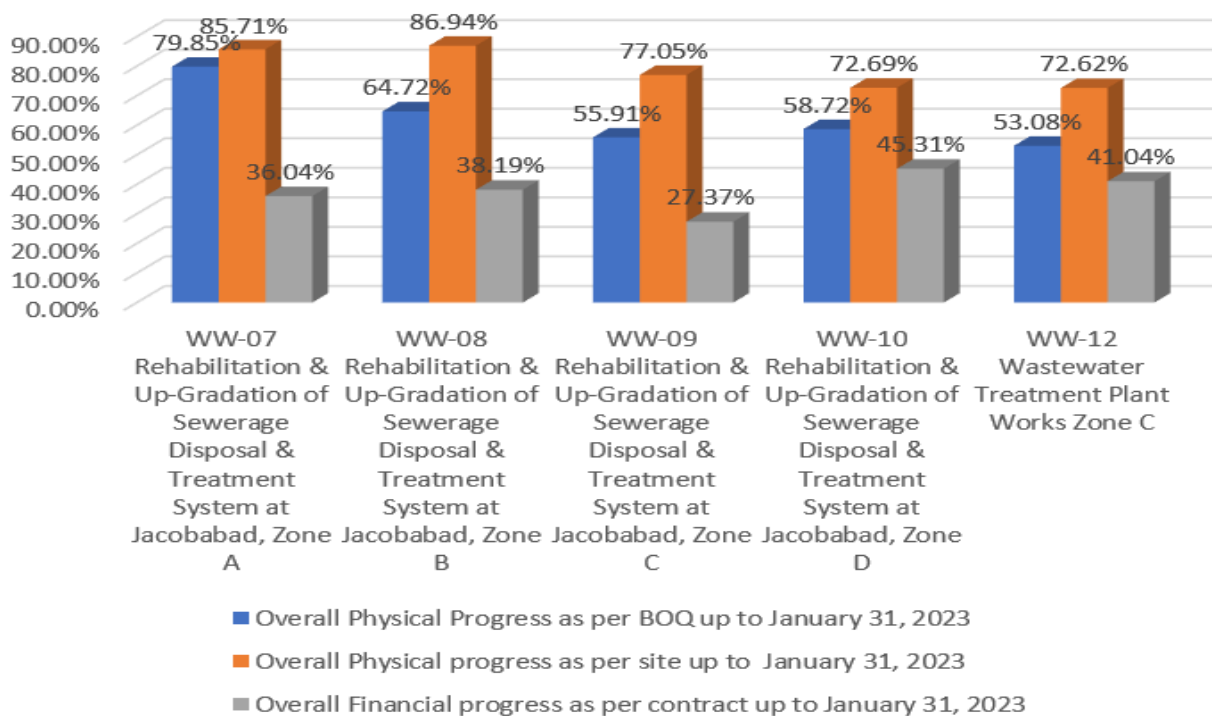


Table 5: Pocket Wise/ Street Wise Progress of Waste Water as of 31<sup>st</sup> January 2023

Packages/ Zone	Pocket Wise Progress					Street Drain Wise Progress			
	Total Numbers of Pockets In each zone	Pocket wise work has started/ In-progress (under 50%)	Pocket wise then 50% work has been done	Complete d & Connected Pocket	Yet not started	Total Streets/ Drains	Completed Streets	In-progress streets	Yet not started
1	2	3	4	5	6	7	8	9	10
WW-07 Zone - A	17	2	3	11	1	816	446	21	349
WW-08 Zone -B	21	2	2	17	0	580	302	4	274
WW-09 Zone -C	11	3	2	6	0	399	261	5	133
WW-10 Zone -D	8	1	1	5	1	344	313	6	25
<b>Total</b>	<b>57</b>	<b>8</b>	<b>8</b>	<b>39</b>	<b>2</b>	<b>2139</b>	<b>1322</b>	<b>36</b>	<b>781</b>

## 6 WATER SUPPLY & SEWERAGE CONNECTIONS

### 6.1 Clamps & Extended Household Connections (Updated by Municipal Committee Jacobabad as on 31.01.2023)

The current position of clamps and extended household connections installed up to 31.01.2023 are given below:

Table 6: Clamps & Extended Connections as of 31<sup>st</sup> January 2023

<b>* Household Connection details of All Water Supply Zones</b>			
<b>S. No.</b>	<b>Zone</b>	<b>Total Registration</b>	<b>Connection Provided by MC Jacobabad after Handing/Taking</b>
01	<b>Zone-01</b>	3445	3295
02	<b>Zone-02</b>	1904	1699
03	<b>Zone-03</b>	3161	2711
04	<b>Zone-04</b>	1700	1422
05	<b>Zone-05</b>	2369	1902
06	<b>Zone-06</b>	3363	1730
07	<b>AWS-3</b> (Missing Street in above different water supply zones)	1062	1062
08	<b>Zone 5 -A</b> (through WS-13)	1566	Nil
<b>Total</b>		<b>18570</b>	<b>13821</b>

### 6.2 Data of Household Connections of Sewer System as of 31<sup>st</sup> January 2023

Table 7: Household Connections of Sewer System as of 31<sup>st</sup> January 2022

<b>ZONE</b>	<b>Previous House connections till 31<sup>st</sup> December 2022</b>	<b>New No. of House connections in the Month of January 2023</b>	<b>Total number of House connections till 31<sup>st</sup> January 2023</b>
<b>A</b>	4261	10	4271
<b>B</b>	2357	50	2407
<b>C</b>	2567	0	2567
<b>D</b>	1564	0	1564
<b>Total</b>			<b>10,809</b>

## 7 FINANCIAL PROGRESS

### 7.1 Status of IPCs Payment up to January 2023 (Running Activities)

Packages Number	Packages Name	Financial Progress (up to 31.01.2023) (in % age)	Total Payment made in the month of January 2023 (PKR)	Total Payment made till 31 <sup>st</sup> January 2023 (PKR)
<b>WW-07</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone A	36.04%	Nil	214,310,132
<b>WW-08</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone B	38.19%	Nil	181,789,619
<b>WW-09</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone C	27.37%	Nil	130,426,692
<b>WW-10</b>	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone D	45.31%	Nil	151,721,839
<b>WW-12</b>	Wastewater Treatment Plant Works Zone C	41.04%	Nil	147,482,590
<b>A&amp;E Firm (Cost revised)</b>	M/s RCC Consultant	83.01%	4,076,100	108,596,333
<b>Total</b>		<b>45.16%</b>	<b>4,076,100</b>	<b>934,327,205</b>



## 8 PICTORIAL OVERVIEW OF WASTE-WATER CONTRACT PACKAGES

WW-07 (Zone-A) Brick masonry of boundary wall work in progress at Revenue Colony Jacobabad



WW-07 (Zone-A) Concrete pouring of Column Footing for boundary wall work in progress at Revenue Colony PS Jacobabad





WW-07 (Zone-B) Brick Masonry of Boundary wall work in progress at Revenue colony PS Jacobabad



WW-07 (Zone-A) RCC Casing work for Raising Main work in progress at Revenue Colony Jacobabad





WW-07 (Zone-A) Laying of RCC Pipeline for Casing work in progress



WW-07 (Zone-A) Back filling of Boundary wall work in progress at Revenue Colony Jacobabad





WW-07 (Zone-A) Dismantling of road for laying RCC Pipe for drain connections to bliss.



WW-08 (Zone B) Excavation of drain work in progress at street No. 1-E8 Gulab Machi Jacobabad





WW-08 (Zone B) Brick Masonry of drain work in progress at Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Brick Masonry of drain work in progress at Street No. 13-D, Al Murtaza Colony Jacobabad





WW-08 (Zone-B) Plaster of Brick Masonry of drain work in progress at street No. 13-D Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Plaster of brick masonry work in progress at street No. 13-D Al Murtaza Colony Jacobabad





WW-08 (Zone-B) Plaster of drain work in progress at Street No. 11-A, Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Plaster of brick masonry work in progress at street No. 11-A Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Concrete Pouring of Sump wall in progress at A Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Brick masonry of drain work in progress at street No. 11-B, Al Murtaza Colony Jacobabad





WW-08 (Zone-B) Sinking the Sump work in progress with the help of Excavator at Al Murtaza Colony Jacobabad



WW-08 (Zone-B) Plaster of Brick masonry of drain type 3 work in progress at Al Murtaza Colony Jacobabad





WW-09 (Zone-C) Cylinders testing of Compression for Sump of Disposal work in progress near Railway Station Jacobabad



WW-12 (Zone-C) Jointing of HDPE500 mm diameter Pipe for Raising Main work is in progress at Shamb-e-Shah to Noor Wah Jacobabad





WW-12 (Zone-C) Excavation for lying HDPE 500mm diameter Pipe for Raising Main work in progress at Shamb-e-Shah to Noor Wah




WW-12 (Zone-C) Raising Main 500 mm diameter PE Pipeline work in progress at Hambi road Jacobabad





## 9 ENVIRONMENTAL COMPLIANCE AT SITE

Regarding environmental compliance and monitoring at site, the draft modified EDF-EMMP document is referred. Monitoring on-site was carried out for each contract package as per the corresponding EMMP. The draft modified EDF-EMMP document is yet to be approved by USAID. The environmental compliance report is separately submitted to USAID.

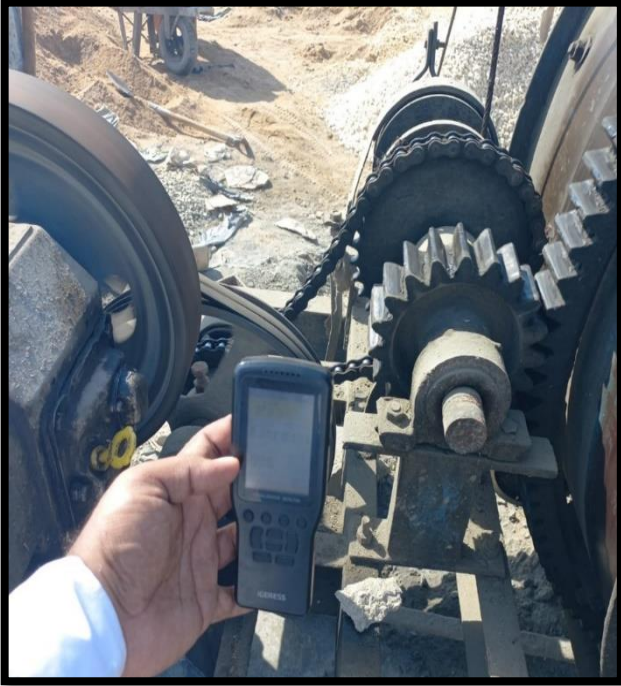

To check the Air Pollution level with the help of Formaldehyde Detector



To check the Noise Pollution level with the help of (Digital Sound level Meter).



Monitoring of Air Pollution level during execution of work at Zone A Yard with the help of Formaldehyde



Monitoring of Air Pollution level with help of Formaldehyde Detector

## **10 PROJECT GRIEVANCES REDRESSAL MECHANISM (GRM) OF SINDH-MSDP**

The Sindh-MSDP is enthusiastic and motivated to address/ resolve the grievances of citizens of Jacobabad, Sindh. It is pivotal for any democratic society that the people (end users) and their ideas be put in first place. This makes the Grievances Redressal a very important task. The Sindh-MSDP effectively ensures the systematic resolution of citizen grievances through a transparent and efficient manner on the fast track. Presently, a dual system is prevailing for Project's Grievances Redressal Mechanism; Pakistan Citizen's Portal (PCP); and MSDP's internal mechanism established at designated Project Support Unit Jacobabad and Project Management Unit. This task demands dedicated and concentrated efforts in the right direction to bring sustainable change. It is not out of place to mention that Sindh-MSDP has embarked effectively for providing higher level of service delivery to urban and peri-urban population of project area for enhanced quality of life.

*Table 8: Complaints Statistics as of 31<sup>st</sup> January 2023*

<b>Pakistan Citizen's Portal (PCP)</b>		
Total Complaints received up to January 2023	Complaints Resolved	In-progress Complaints
<b>89</b>	<b>89</b>	<b>0</b>
<b>Grievances Redressal Mechanism (GRM) for Project Activities</b>		
<b>97</b>	<b>91</b>	<b>06</b>

The above statistical illustration is an overall glimpse of grievances received and resolved through Pakistan Citizen Portal (PCP) and Grievances Redressal Mechanism (GRM) during the month of January 2023 regarding service delivery. It is aimed that the MSDP team will continue to work dedicatedly day in and day out to ensure the rapid Redressal of Citizens Grievances.

In order to address the issues highlighted by general public regarding connectivity, de-silting, placement of slabs on drains and lifting of dismantled/waste material from site etc. the five (05) Sub Engineers of Program Support Unit have been mobilized. They visit the field on regular basis and report the on-ground situation on a checklist/ proforma. The Assistant Director (Execution) Program Support Unit compiles the observations and shares the same with Resident Engineer, RCC Consultant for their timely redressal.

## 10.1 Grievance's Redressal Mechanism (GRM)

Table 9: Summary Sheet of GRM

### Grievances Redressal Mechanism (GRM) SUMMARY SHEET

Progress up to 31<sup>st</sup> January 2023

S. No.	NATURE /CATEGORY OF COMPLAINT	TOTAL COMPLAINTS RECEIVED			TOTAL COMPLAINTS RESOLVED			TOTAL COMPLAINTS PENDING			REASONS OF PENDENCY	REMARKS
		Jan 2023	Sep 2021 to Jan 2023	Total	Jan 23	Sep 2021 to Jan 2023	Total	Jan 23	Sep 2021 to Jan 2023	Total		
1	2	3	4	5	6	7	8	9	10	11	12	13
1	Water Supply	0	11	11	0	11	11	0	0	0	Work in Progress	RCC was requested to resolve pending GRM at war-footing basis
2	Waste Water	0	86	86	0	80	80	0	6	6		
<b>Grand Total</b>		<b>0</b>	<b>97</b>	<b>97</b>	<b>0</b>	<b>91</b>	<b>91</b>	<b>0</b>	<b>6</b>	<b>6</b>		

## 10.2 Summary of daily field visit reports of all packages by Sub Engineers

Summary of daily field visit reports of all contract packages

(WW-07, 08, 09 & 10)

Table 10: Summary of Daily Field Visit

S. No.	Name of Sub Engineer	Name of Zone	Total sites visited by concerned Sub Engineer
1.	Mr. Abrar Ahmed Thaheem & Mr. Anis-ur-Rehman Khoso	<b>WW-07 (Zone A)</b>	108
2.	Mr. Mudassar Ali Rajput	<b>WW-08 (Zone B)</b>	70
3.	Mr. Asghar Abbas Sadhayo	<b>WW-09 (Zone C)</b>	70
4.	Mr. Tufail Ahmed Soomro	<b>WW-10 (Zone D)</b>	74
<b>Total</b>			<b>322</b>



## 11 MEETINGS

### 11.1 Meeting with USAID Delegate at Program Management Unit Sindh Municipal Services Delivery Program

On 18<sup>th</sup> January 2023, USAID Delegation comprised of Mr. Michael Rossman Deputy Mission Director USAID/Pakistan, Mr. Hafeez Samo, Ms. Sarah Pervaiz and Mr. Adeel Ahmed Shaikh Program Management Specialist (Engineering) visited the Sindh MSDP office. Program Director Municipal Services Delivery Program Mr. Shah Zaman Khuhro welcomed USAID Delegation. The Program Director briefed the delegation about the program and discussed the administrative, financial, strategic challenges and future work plans of Sindh MSDP. The USAID Delegation expressed satisfaction on the progress of project and assured continued support of USAID.



Further, in a meeting with USAID Delegation the Program Director also briefed on the efforts of MSDP team to achieve the progress. Mr. S.M Shakaib Director General (Works) MSDP, Ms. Uzaima Nasir Director (Finance & Compliance) MSDP, Mr. M. Aslam Memon Assistant Director (HRD) MSDP and Ms. Saba Zehra Assistant Director (GIS/MIS) MSDP attended the meeting.







## 11.2 Progress Review Meeting

A progress review meeting was held on 31<sup>st</sup> January 2023, in the Committee room of PMU Sindh MSDP under chairmanship of Director General (Works). Mr. Babar Ismail Palijo Deputy Director (Design) MSDP, Ms. Saba Zehra Assistant Director (GIS/MIS), and Mr. Adeel Ahmed Shaikh Program Management Specialist (Engineering) USAID/Pakistan were present in the meeting.

Mr. Shafi Muhammad Lakho Team Leader M/s. RCC Consultants the Engineer of the Program, Mr. Basheer Ahmed Resident Engineer M/s RCC Consultants, Mr. Hussain Bux Engineer M/s RCC Consultants, Mr. Asif Rind Project Manager M/s Shafqat Traders, Mr. Rashid Owner of M/s M. Hasni Builders, Mr. Nisar A Khan N.K & Company, Mr. Muhabbat Ali Mangi Project Manager M/s NK & Co. Mr. Yosef Owner of M/s K.K & Brothers, Mr. Hamid Naveed M/s K.K & Brothers, Mr. M. Mumtaz Tunio Project Manager WW-09 & WW-10, and Mr. Muhammad Iqbal Shaikh owner of M/s M. Iqbal Shaikh & Co attended the meeting. The Director General (Works) Sindh Municipal Services Delivery Program (MSDP) reviewed the progress of all ongoing works of wastewater packages and conveyed that the follow-up meetings for the review of site activities and issues will be held on priority basis to accomplish the targets on time.



The chair directed to expedite the progress of remaining works of waste water and follow spent plan/work plan for the completion of the project. After detailed deliberation, the chair asked M/s RCC Consultants that all contractors of package WW-07, WW-08, WW-09, WW-10, WW-11 & WW-12 are requested to submit a weekly activity plan of remaining works by 8<sup>th</sup> February 2023. The Director General (Works) MSDP also reiterated that contractor will submit pocket wise handing over of drains to Municipal Committee Jacobabad. During the meeting Director General (Works) MSDP emphasized the close coordination on daily basis between all Project Managers and Project Support team is needed to get the possible outcome/targets.



## 12 TRAINING

### 12.1 Research & Training Wing LED Public Sector Development Program/Project Management Case Study Based Training Module

On 4<sup>th</sup> January 2023, Research & Training Wing Led Public Sector Development Program/Project Management Case Study-based Training Module for 6<sup>th</sup> CSTP 2022 was held at Sindh MSDP in collaboration with TMR Wing, Services General Administration & Coordination Department, Government of Sindh. The group comprised of four (04) PMS Probationers including Mr. Tariq Ahmed Junejo, Ms. Marvi Leghari, Ms. Summiya Khan, and Mr. Syed Taha Ahmed.

Program Director of MSDP welcomed PMS Probationers of 6<sup>th</sup> CSTP for their case studies at Sindh MSDP office. Being a focal person Director General (Works) MSDP conducted interactive case study session with group of PMS probationers. Subsequently, Team leader Mr. Tariq Ahmed Junejo thanked Program Director MSDP, Director General (Works) MSDP and his team for arranging a collaborative and interactive session. Deputy Director (Design), Deputy Director (Execution) & Assistant Director (HRD) Sindh MSDP were also present in the training module.









**MSDP**

Municipal Services Delivery Program



**USAID**  
FROM THE AMERICAN PEOPLE

# Program Management Unit

Sindh Municipal Service Delivery Program

D-18 Block-2 | Clifton Karachi | Pakistan

Tel No. 021-35810017-18 | Fax No. 021-35810019

[www.msdp.sindh.gov.pk](http://www.msdp.sindh.gov.pk)
