

Sindh Municipal Services Delivery Program

MONTHLY PROGRESS REPORT

(MARCH 2023)



MSDP
Sindh Municipal Service Delivery Program



USAID
FROM THE AMERICAN PEOPLE

Program Director:

Raja Shah Zaman Khuhro

Scheme Number:

(As reflected in Provincial ADP Book)

ADP No. 2635/2022-23

Program Started: 2012

Execution of Work Started:

March 2014 end date 30th September 2023

House No. D-18, Block-2 Kehkashan Clifton, Karachi
www.msdp.sindh.gov.pk | Telephone # 021-35810017-18 | Fax # 021-35810019

Prepared by: Monitoring & Evaluation Section MSDP
Verified by: Technical & Finance Section MSDP
Submitted by: Monitoring & Evaluation Section MSDP
Submitted to: P&DD, M&E Cell and USAID/PAKISTAN
Program Director: Raja Shah Zaman Khuhro

Contents

1	INTRODUCTION	6
2	SUMMARY OF PROJECT ACTIVITIES (ALL COMPONENTS)	7
3	OVERALL PROGRESS OF THE PROGRAM	10
4	PROGRESS OF WATER SUPPLY PROJECT	10
5	PROGRESS OF WASTE WATER PROJECT	11
6	WATER SUPPLY & SEWERAGE CONNECTIONS	13
7	FINANCIAL PROGRESS	14
8	PICTORIAL OVERVIEW OF WASTE-WATER CONTRACT PACKAGES	15
9	ENVIRONMENTAL COMPLIANCE AT SITE	20
10	PROJECT GRIEVANCES REDRESSAL MECHANISM (GRM) OF SINDH-MSDP	21
11	MEETINGS	23
12	SEMINAR	27
13	SITE VISITS	28

List of Tables

Table 1: Summary of Project Activities	7
Table 2: Overall Progress of the Program	10
Table 3: Progress of Water Supply Project	10
Table 4: Physical Progress of Waste Water Project (Component wise) as of 31 st March 2023 .	11
Table 5: Pocket Wise/ Street Wise Progress of Waste Water as of 31 st March 2023	12
Table 6: Clamps & Extended Connections as of 31 st March 2023	13
Table 7: Household Connections of Sewer System as of 31 st March 2023	13
Table 8: Complaints Statistics as of 31 st March 2023	21
Table 9: Summary Sheet of GRM	22
Table 10: Summary of Daily Field Visit	22

Abbreviations

Acronyms	
MSDP	Municipal Services Delivery Program
USAID	United States Agency for International Development
WS	Water Supply
C&EHHC	Clamps & Extended Household Connections
WW	Waste Water
LGSA	Local Government Strengthening Activity
EAS (DPC)	Energy Audit Study of Dhabeji Pumping Complex
IPC	Interim Payment Certificate
GRM	Grievances Redressal Mechanism
PCP	Pakistan Citizen's Portal
TCI	Techno Consultant International
PMU	Program Management Unit
PSU	Program Support Unit
IAP	Interim Payment Application
MCJ	Municipal Committee Jacobabad
EM	Equipment & Machinery
BOQ	Bill of Quantities
AWS	Additional Water Supply

1 INTRODUCTION

This report reflects the Monthly Progress of March 2023, prepared by Sindh Municipal Services Delivery Program (MSDP). The report furnishes updates as of 31st March 2023.

Background of the Project

Name of Program	Sindh Municipal Services Delivery Program		
Program Goal	Sustained improvement in municipal service delivery to effectively address the basic needs of citizens located in small and medium towns		
Foundation Year	2012 Activity Agreement signed on 25 th April 2012 between USAID/Pakistan & Government of Sindh		
Completion Year	September 2023 (Extension was previously granted in the year 2020)		
Executing Partners	Government of Sindh		
Funds Committed	USAID	USD 66.00 Million	
	GoS	PKR 926.5 Million	
Total Funds	PKR 6,668.55 million		
Organizational Structures	Program Steering Committee-PSC	Program Management Unit-PMU	Program Support Unit-PSU
Targeted Towns Components	1. Jacobabad 2. Johi 3. KN Shah 4. Shahdadkot 5. Qambar 6. Mehar		
	Infrastructure Development Component	Components Type-A Water Supply	Infrastructure Development Component Rehabilitation & Improvement of Water Supply System in Jacobabad has been completed & handed over to MCJ on 14.4.2021
		Type-B Sanitation (Waste Water)	Work for the Rehabilitation and Upgradation of Waste water system in Jacobabad town has also started from March 2020 and achieved progress up to 80%.
		Type-C Solid Waste Management	Equipment and Machinery were handed over to Municipal Committee Jacobabad on 22.06.2019 in the Numaish Ground, Jacobabad for handling of Solid Waste. Out of this fleet, after retaining the machinery for Jacobabad, remaining were distributed to other cities i.e. Jacobabad (40), Thull (12), Garhi Khairo (11), Shahdadkot (09), Sehwan (09) and Tangwani (07).
	Soft Component	LGSA	The reports & manuals developed under LGSA has been disseminated to relevant stakeholders (P&DD, LG&HTP, Training & Management wing of SGA&CD, R&T Wing P&DD, Sindh Civil Services & Local Govt. Academy, Deputy Commissioner Jacobabad, Administrator MC Jacobabad, MCs of six towns i.e. Jacobabad, Qambar, Shahdadkot, K.N Shah, Mehar and Johi.
Energy Audit Study of DPC		Work initiated on 3 rd March 2021 and all the deliverables are completed on 20 th October 2021.	

2 SUMMARY OF PROJECT ACTIVITIES (ALL COMPONENTS)

The overall consolidated status of each awarded contract is given below:

Table 1: Summary of Project Activities

Package Code	Package Name	Name of Construction Contractor	Contract Cost in	Date of Commencement	Date of completion extended up to	Status
INFRASTRUCTURE DEVELOPMENT: TYPE A (WATER SUPPLY)						
WS-01	Water Intake and Storage System	M/s Samad Khan Babar & Co	332,142,149	March 13 th , 2014	May 31 st , 2017	Completed Handed Over to MCJ on 22.05.2017
WS-02	High Lift Pumping System and Rising Mains	M/s Shaikh Baz Khan & Brothers	639,589,414	March 13 th , 2014	November 17 th , 2016	Completed Handed Over to MCJ on 22.05.2017
WS-03	Water Supply Transmission Loop	M/s Crescent Construction Company & KSB Pumps Company Ltd.	256,507,205	March 13 th , 2014	March 31 st , 2017	Completed Handed Over to MCJ on 14.04.2021
WS-04	Water Distribution System Zone 1 & 2	M/s MAX-RITE Global Technologies (Pvt.) Ltd.	206,725,598	September 27 th , 2017	November 30 th , 2019	Completed Handed Over to MCJ on 14.04.2021
WS-05	Water Distribution System Zone 3 & 4	M/s Matracon Pakistan (Pvt.) Limited	220,798,980	September 26 th , 2014	March 22 nd , 2019	Completed Handed Over to MCJ on 14.04.2021
WS-06	Water Distribution System Zone 5 & 6	M/s Khan Mohammad & Co.	153,129,329	November 21 st , 2014	March 29 th , 2019	Completed Handed Over to MCJ on 14.04.2021
WS-15	Rehabilitation & Extension of Existing Water Treatment Plant at Jacobabad	M/s Mohammad Iqbal Shaikh & Co.	201,894,354	November 11 th , 2015	March 29 th , 2019	Completed Handed Over to MCJ on 14.04.2021
EM-11	Procurement and Installation of E&M Works	M/s Engineering Links International	125,560,528	May 18 th , 2017	March 22 nd , 2019	Completed Handed Over to MCJ on 14.04.2021

INFRASTRUCTURE DEVELOPMENT: TYPE B (WASTE WATER)							
Package Code	Package Name	Name of Construction Contractor	Contract Cost	Expected Completion Cost	Date of Commencement	Date of completion/ extended up to	Status
WW-07	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone A	M/s Shafqat Traders & Mohammad Hasni Builders (JV)	594.634 Million	419.464 Million	February 11 th , 2020	30 th June, 2023*	In Progress
WW-08	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone B	M/s N.K & Co	476.042 Million	343.406 Million	February 7 th , 2020	30 th June, 2023*	In Progress
WW-09	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone C	M/s Kaim Khani & Brothers	476.566 Million	317.048 Million	February 7 th , 2020	30 th June, 2023*	In Progress
WW-10	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone D	M/s Kaim Khani & Brothers	334.822 Million	334.758 Million	February 11 th , 2020	30 th June, 2023*	In Progress
WW-12	Wastewater Treatment Plant Works Zone C	M/s Mohammad Iqbal Shaikh & Co.	359.38 Million	455.445 Million	February 4 th , 2021	30 th June, 2023*	In Progress
WW-16	Enhancement of Sewerage Flow from Main Pumping House of Zone-A, B, C to their Oxidation Pond for Treatment purpose in Jacobabad	M/s Mohammad Iqbal Shaikh & Co.	394.707 Million	394.800 Million	February 10 th , 2023	August 11 th , 2023	In progress

*EoTs are under process

INFRASTRUCTURE DEVELOPMENT: TYPE C (SOLID WASTE MANAGEMENT)

Package Code	Package Name	Name of Construction Contractor	Contract Cost	Date of Commencement	Date of completion extended up to	Status
EM-14	Procurement of Equipment and Machinery for Improvement of Solid Waste Management System in Jacobabad	M/s Colibrative Heavy Industries (Pvt.) Limited	188,617,000	June 13 th , 2018	June 22 nd , 2019	Completed All the Equipment and Vehicles were distributed among Local Councils of Jacobabad, Thull, Ghari Khero, Shahdaktot, Sehwan & Tangwani towns.

SOFT COMPONENT

Package Code	Package Name	Name of Construction Contractor	Contract Cost in	Date of Commencement	Date of completion extended up to	Status
LGSA	Local Government Strengthening Activity	M/s MDC (Pvt.) Ltd.	79,998,910	October 22 nd , 2019	August 31 st , 2021	Completed
	Hiring of Training Consultant for required International Trainings for Capacity Building	M/s Stalwart Design Concepts	290,000	August 11 th , 2022	September 13 th , 2022	Training Deliverables/ToRs have been Completed
EAS of DPC	Energy Audit Study of the Dhabeji Pumping Station of KW&SB	M/s Techno-Consult International (Pvt.) Ltd. (Lead Firm), M/s Eleken Associates (JV Partner) & M/s WEE Pros GmbH- Germany (Associates)	49,200,400	March 3 rd , 2021	October 20 th , 2021	Completed

3 OVERALL PROGRESS OF THE PROGRAM

Table 2: Overall Progress of the Program

S. No.	Components	Cost (PKR)	Status	Physical Progress	Weightage	Physical Progress as per weightage in %
A	INFRASTRUCTURE DEVELOPMENT					
i	Rehabilitation & Improvement of Water Supply System in Jacobabad	2,141,893,087	Completed	100%	44.15%	44.15%
ii	Rehabilitation & Improvement of Sewerage Disposal & Treatment System Jacobabad	2,391,590,567	In Progress	79.96%	49.30%	39.42%
iii	Solid Waste Management	188,617,000	Completed	100%	3.89%	3.89%
B	SOFT COMPONENT					
i	Local Government Strengthening Activity	80,072,910	Completed	100%	1.65%	1.65%
ii	Energy Audit Study Of KW&SB Dhabeji Pumping Complex	49,200,400	Completed	100%	1.01%	1.01%
	TOTAL	4,851,373,964				90.12%
Overall physical progress of Sindh MSDP is: 90.12%						

4 PROGRESS OF WATER SUPPLY PROJECT

Table 3: Progress of Water Supply Project

Package Code	Package Name	Physical Progress	Financial Progress	Status
WS-01	Water Intake and Storage System	100%	100%	22.05.2017
WS-02	High Lift Pumping System and Rising Mains	100%	100%	
WS-03	Water Supply Transmission Loop	100%	100%	Completed & handed over to MCJ on 14.04.2021
WS-04 (R)	Water Distribution System Zone 1 & 2	100%	100%	
WS-05	Water Distribution System Zone 3 & 4	100%	100%	
WS-06	Water Distribution System Zone 5 & 6	100%	100%	
WS-15	Rehabilitation & Extension of Existing Water Treatment Plant at Jacobabad	100%	100%	
EM-11	Procurement and Installation of E&M Works	100%	100%	

5 PROGRESS OF WASTE WATER PROJECT

The waste water components are currently in execution phase under the supervision of M/s RCC Consultant who acts as the Engineer and TCI appointed by the USAID as Third-Party monitoring.

5.1 Physical & Financial Progress of Waste Water Component

The detailed progress under each sub-component of waste water is given as under:

Table 4: Physical Progress of Waste Water Project (Component wise) as of 31st March 2023

Packages Number Code	Packages Name	Physical Progress as per BOQ up to 31st March 2023	Overall Physical Progress as per Site up to 31st March 2023	Overall Financial Progress as per contract up to 31st March 2023
WW-07	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-A at Jacobabad,	79.39%	85.77%	36.04%
WW-08	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-B at Jacobabad,	67.36%	86.94%	39%
WW-09	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-C at Jacobabad,	86.82%	77.05%	28.84%
WW-10	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System of Zone-D at Jacobabad,	58.80%	72.69%	51.83%
WW-12	Wastewater Treatment Plant Works Zone D	77.35%	77.35%	78.28%
Overall Physical Progress		73.94%	79.96%	46.79%

Note: Overall Physical Progress based on the basis of workable quantities as per site identified by the Engineer-RCC Consultant.

Physical Progress as per BoQ, Site and Financial Progress in Graph

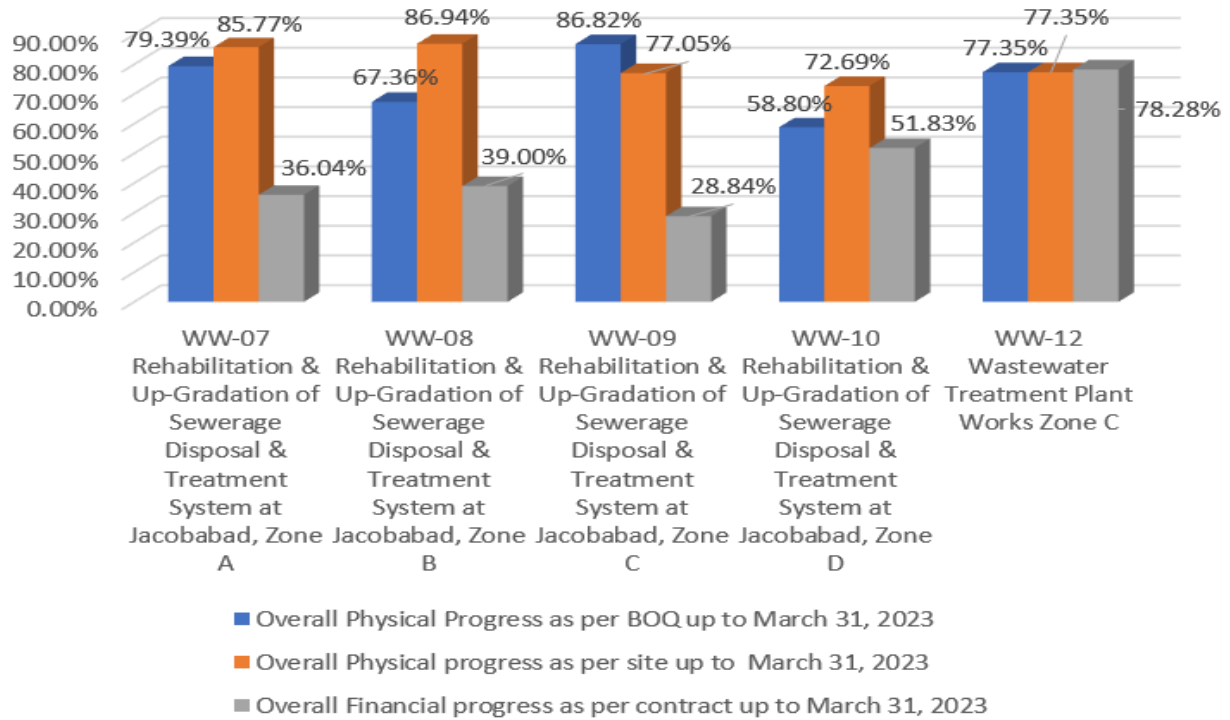


Table 5: Pocket Wise/ Street Wise Progress of Waste Water as of 31st March 2023

Packages/ Zone	Pocket Wise Progress					Street Drain Wise Progress			
	Total Numbers of Pockets In each zone	Pocket wise work has started/ In- progress (under 50%)	Pocket wise then 50% work has been done	Complete d & Connected Pocket	Yet not started	Total Streets/ Drains	Completed Streets	In- progress streets	Yet not started
1	2	3	4	5	6	7	8	9	10
WW-07 Zone - A	17	2	3	11	1	816	449	10	357
WW-08 Zone -B	21	2	2	17	0	580	312	8	260
WW-09 Zone -C	11	3	2	6	0	399	261	5	133
WW-10 Zone -D	8	1	1	5	1	344	313	6	25
Total	57	8	8	39	2	2139	1335	29	775

6 WATER SUPPLY & SEWERAGE CONNECTIONS

6.1 Clamps and Extended Household Connections (updated by Municipal Committee Jacobabad as on 31.03.2023)

The current position of clamps and extended household connections installed up to 31.03.2023 are given below:

Table 6: Clamps & Extended Connections as of 31st March 2023

* Household Connection details of All Water Supply Zones			
S. No.	Zone	Total Registration	Connection Provided by MC Jacobabad after Handing/Taking
01	Zone-01	3445	3295
02	Zone-02	1904	1699
03	Zone-03	3161	2711
04	Zone-04	1700	1422
05	Zone-05	2369	1902
06	Zone-06	3363	1730
07	AWS-3 (Missing Street in above different water supply zones)	1062	1062
08	Zone 5 -A (through WS-13)	1566	Nil
Total		18570	13821

6.2 Data of Household Connections of Sewer System as of 31st March 2023

Table 7: Household Connections of Sewer System as of 31st March 2023

ZONE	Previous House connections till 28th February 2023	New No. of House connections in the Month of March 2023	Total number of House connections till 31st March 2023
A	4296	0	4296
B	2417	0	2417
C	2567	0	2567
D	1564	0	1564
Total			10,844

7 FINANCIAL PROGRESS

7.1 Status of IPCs Payment up to March 2023 (Running Activities)

Packages Number	Packages Name	Financial Progress (up to 31.03.2023) (in % age)	Total Payment made in the month of March 2023 (PKR)	Total Payment made till 31st March 2023 (PKR)
WW-07	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone A	36.04%	Nil	214,310,132
WW-08	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone B	39%	Nil	185,645,698
WW-09	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone C	28.84%	Nil	137,426,692
WW-10	Rehabilitation & Up-Gradation of Sewerage Disposal & Treatment System at Jacobabad, Zone D	51.83%	Nil	173,551,339
WW-12	Wastewater Treatment Plant Works Zone C	78.28%	Nil	281,336,014
A&E Firm (Cost revised)	M/s RCC Consultant	90.42%	6,361,000	118,300,333

8 PICTORIAL OVERVIEW OF WASTE-WATER CONTRACT PACKAGES

WW-07 (Zone-A): Sump Sinking work is in progress



WW-07 (Zone-A): Work in progress at Phool Bagh Sumping Station



WW-07 (Zone-A): Excavation of footing for boundary wall of Phool Bagh disposal work in progress




WW-10 (Zone-D): Formwork, water curing, and repair is in progress at Pachuhu Sump



WW-10 (Zone-D): Reinforcement and formwork for Sump work is in progress



WW-10 (Zone-D): Sinking for disposal work is in progress at Talani area

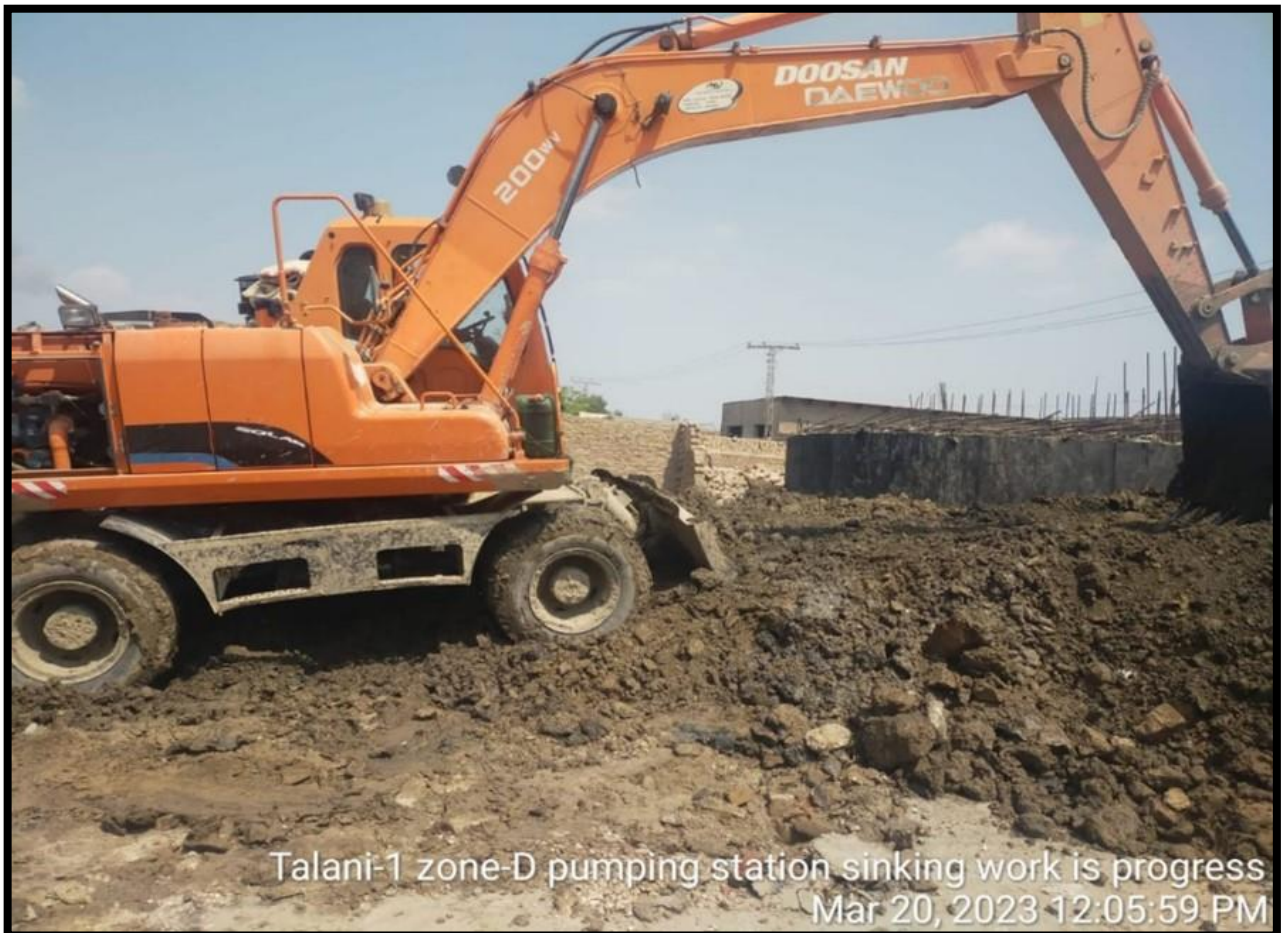

WW-12: Hydrostatic pressure test is in progress



WW-12: Jointing of 500mm dia pipe for Rising main is in progress at Shamb-e-Shah to Noor Wah



WW-12: Jointing of 500mm dia pipe for Rising main is in progress at Shamb-e-Shah to Noor Wah



WW-12: Jointing of 500mm dia pipe for Rising main is in progress at Shamb-e-Shah to Noor Wah



9 ENVIRONMENTAL COMPLIANCE AT SITE

Regarding environmental compliance and monitoring at site, the draft modified EDF-EMMP document is referred. Monitoring on-site was carried out for each contract package as per the corresponding EMMP. The draft modified EDF-EMMP document is yet to be approved by USAID. The environmental compliance report is separately submitted to USAID.



To check the Air Pollution level with the help of Formaldehyde Detector



To check the Noise Pollution level with the help of (Digital Sound level Meter).



Monitoring of Air Pollution level during execution of work at Zone A Yard with the help of Formaldehyde



Monitoring of Air Pollution level with help of Formaldehyde Detector

10 PROJECT GRIEVANCES REDRESSAL MECHANISM (GRM) OF SINDH-MSDP

The Sindh-MSDP is enthusiastic and motivated to address/ resolve the grievances of citizens of Jacobabad, Sindh. It is pivotal for any democratic society that the people (end users) and their ideas be put in first place. This makes the Grievances Redressal a very important task. The Sindh-MSDP effectively ensures the systematic resolution of citizen grievances through a transparent and efficient manner on the fast track. Presently, a dual system is prevailing for Project's Grievances Redressal Mechanism; Pakistan Citizen's Portal (PCP); and MSDP's internal mechanism established at designated Project Support Unit Jacobabad and Project Management Unit. This task demands dedicated and concentrated efforts in the right direction to bring sustainable change. It is not out of place to mention that Sindh-MSDP has embarked effectively for providing higher level of service delivery to urban and peri-urban population of project area for enhanced quality of life.

Table 8: Complaints Statistics as of 31st March 2023

Pakistan Citizen's Portal (PCP)		
Total Complaints received up to March 2023	Complaints Resolved	In-progress Complaints
90	89	01
Grievances Redressal Mechanism (GRM) for Project Activities		
99	98	01

The above statistical illustration is an overall glimpse of grievances received and resolved through Pakistan Citizen Portal (PCP) and Grievances Redressal Mechanism (GRM) during the month of March 2023 regarding service delivery. It is aimed that the MSDP team will continue to work dedicatedly day in and day out to ensure the rapid Redressal of Citizens Grievances.

In order to address the issues highlighted by general public regarding connectivity, de-silting, placement of slabs on drains and lifting of dismantled/waste material from site etc. the five (05) Sub Engineers of Program Support Unit have been mobilized. They visit the field on regular basis and report the on-ground situation on a checklist/ proforma. The Assistant Director (Execution) Program Support Unit compiles the observations and shares the same with Resident Engineer, RCC Consultant for their timely redressal.

10.1 Grievance's Redressal Mechanism (GRM)

Table 9: Summary Sheet of GRM

Grievances Redressal Mechanism (GRM) SUMMARY SHEET

Progress up to 31st March 2023

S. No.	NATURE /CATEGORY OF COMPLAINT	TOTAL COMPLAINTS RECEIVED			TOTAL COMPLAINTS RESOLVED			TOTAL COMPLAINTS PENDING			REASONS OF PENDING	REMARKS
		Mar 2023	Sep 2021 to Mar 2023	Total	Mar 23	Sep 2021 to Mar 2023	Total	Mar 23	Sep 2021 to Mar 2023	Total		
1	2	3	4	5	6	7	8	9	10	11	12	13
1	Water Supply	0	11	11	0	11	11	0	0	0	Work in Progress	RCC was requested to resolve pending GRM at war-footing basis
2	Waste Water	0	88	88	0	87	87	1	1	1		
Grand Total		0	99	99	0	98	98	1	1	1	1	

10.2 Summary of daily field visit reports of all packages by Sub Engineers

Summary of daily field visit reports of all contract packages

(WW-07, 08, 09 & 10)

Table 10: Summary of Daily Field Visit

S. No.	Name of Sub Engineer	Name of Zone	Total sites visited by concerned Sub Engineer
1.	Mr. Abrar Ahmed Thaheem & Mr. Anis-ur-Rehman Khoso	WW-07 (Zone A)	290
2.	Mr. Mudassar Ali Rajput	WW-08 (Zone B)	470
3.	Mr. Asghar Abbas Sadhayo	WW-09 (Zone C)	93
4.	Mr. Tufail Ahmed Soomro	WW-10 (Zone D)	78
Total			931

11 MEETINGS

11.1 Community awareness meeting with representatives of USAID HANDS

A community awareness meeting was held on 16th March 2023, in the USAID HANDS office Jacobabad. The agenda of the meeting was to formulate a strategy on how to educate local community regarding waste water ongoing works in the city. Mr. Babar Hussain Sarki Assistant Director (Design/Incharge) Program Support Unit Sindh Municipal Services Delivery Program, and representative of USAID HANDS Mr. Waheed Abro Manager (Technical), Mr. Ishfaqe Mahesar Assistant Manager, Mr. Iqbal Naich Team Leader Social Mobilization were present in the meeting. It was agreed to resolve the issues impeding the execution works in the field on priority basis and community awareness session will be organized on regular basis through social mobilization of local inhabitants regarding proper utilization of water & sanitation services provided to them.



11.2 Meeting with USAID Delegation at Program Management Unit Sindh Municipal Services Delivery Program

On 18th March 2023, USAID Delegation comprises of Mr. Reed Aeschliman Mission Director, Mr. James Fleming Director, Ms. Sarah Pervaiz Adviser and Mr. Adeel Ahmed Shaikh Program Management Specialist (Engineering) USAID/Pakistan visited the Sindh MSDP office.

Syed Hassan Naqvi Chairman, Planning & Development Board, Mr. Muhammad Asghar Memon Chief Economist Planning & Development Department and Program Director Municipal Services Delivery Program Raja Shah Zaman Khuhro welcomed USAID Delegation. The Program Director briefed the delegation about the program and discussed the administrative, technical, financial, strategic challenges and future work plans of Sindh Municipal Services Delivery Program.



The USAID Delegation expressed satisfaction with the progress of the project and assured continued support of USAID. Further, in a meeting with USAID Delegation the Program Director briefed regarding the efforts of MSDP team to achieve progress. Syed Muhammad Shakaib Director General (Works) MSDP, Ms. Uzaima Nasir Director (Finance & Compliance) MSDP attended the meeting.





The Progress of the Sindh MSDP program was appreciated by USAID team. Mr. Reed Aeschliman Mission Director USAID/Pakistan presented souvenir to the Chairman P&D Board and awarded Appreciation Certificates to the Chief Economist, P&DD, Program Director MSDP, Director General (Works) MSDP and all the team members of MSDP project as an acknowledgement to the unrelenting efforts and continuous dedication to complete the Key Performance Indicators of the project.



11.3 Coordination Committee Meeting of USAID-Water Governance

On 21st March 2023, the first Coordination committee meeting of USAID-Water Governance for Sindh Activity was held under the Chairmanship of Deputy Commissioner Mr. Muhammad Yousif Shaikh at Deputy Commissioner office Jacobabad. Mr. Babar Hussain Sarki Assistant Director (Design/Incharge) Program Support Unit MSDP Jacobabad, Mr. Waqar Ali Kalwar Assistant Director (Execution), District Health Officer Jacobabad, officials of Municipal Committee Jacobabad and USAID-HNADS's representative Mr. Touseef Latif Chief of Party, Mr. Waheed Abro Manager Technical, Mr. Ishfaque Mahesar Assistant Manager Electrical Mr. Iqbal Naich Team Leader Social Mobilization were present in the meeting.




At the outset, Deputy Commissioner Jacobabad welcomed the participants and especially thanked the representatives of Sindh MSDP and USAID HANDS team for consistently attending the meeting and contributing through useful suggestions. Incharge Program Support Unit Sindh MSDP Jacobabad briefed them about the program and discussed the technical, financial, and strategic challenges and future work plans of Sindh MSDP. The objective of the meeting was to review the water governance activities, overall progress of the program and to discuss and sort out the important issues being faced by the program teams.



12 SEMINAR

12.1 World Water Day Seminar

On 22nd March 2023, the World Water Day Seminar for awareness of people in Jacobabad on importance of water was organized by USAID/HANDS Water Governance for Sindh Activity Jacobabad. Mr. Babar Hussain Sarki Assistant Director (Design/Incharge PSU Jacobabad, Mr. Waqar Ali Kalwar Assistant Director (Execution) of PMU-Sindh Municipal Services Delivery Program and representative of USAID/HANDS were present in the seminar which included Mr. Mr. Touseef Latif Chief of Party, Mr. Waheed Abro Manager Technical, Mr. Ishfaqe Mahesar Assistant Manager Electrical Mr. Iqbal Naich Team Leader Social Mobilization. A large number of participants from different stakeholders, local community residents, civil society members and NGOs personnel attended the World Water Day Seminar at Jacobabad.

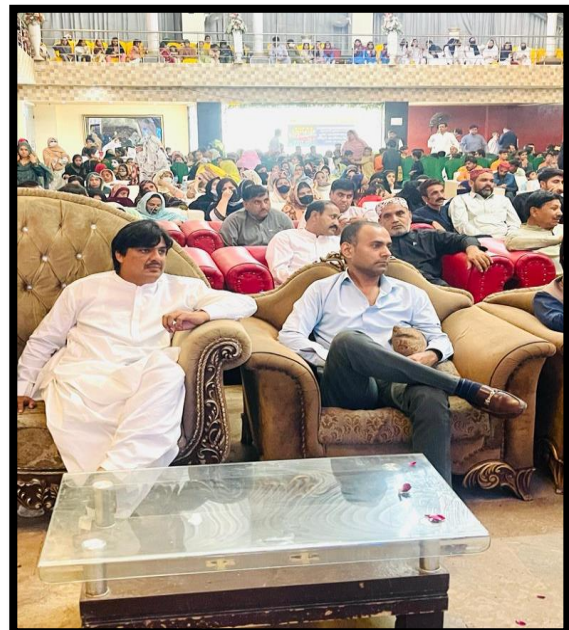

13 SITE VISITS

13.1 Visit of contract packages of WW-08, WW-10 and WW-12

The team Program Support Unit MSDP Jacobabad made a field visit of various contract packages including (ZONE-B) WW-08 Murtaza Colony, (Zone-C) WW-12 Quetta Road highway and (Zone-D) WW-10 Pachuhu Goath Waste Water Pumping Station during the month of March 2023. The purpose of visit was to oversee and review the progress and on-going activities such as Tertiary Drains and Construction of Sump work, Rising Main Pipeline Jointing works and Formation of Sump works carried out through MSDP program at Jacobabad. Mr. Bashir Ahmed, Resident Engineer M/s RCC Consultants along with his filed formation and Contractors of concerned Zones were present during the visit. Mr. Babar Hussain Sarki Assistant Director (Design/Incharge PSU) MSDP team inspected the works at site and compelled the MSDP and M/s RCC Consultant teams for timely completion of all remaining activities on priority basis.





MSDP

Municipal Services Delivery Program



USAID
FROM THE AMERICAN PEOPLE

Program Management Unit

Sindh Municipal Service Delivery Program

D-18 Block-2 | Clifton Karachi | Pakistan

Tel No. 021-35810017-18 | Fax No. 021-35810019

www.msdp.sindh.gov.pk
